

Work Order ID 138374

Tuesday, October 27, 2015 11:27:21 AM

138374

Page 1

Item ID: D2432

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Bearpaw 19" X 24"

Start Date: 10/26/2015 Start Qty: 18.00

18

Cust Item ID:

Required Date: 10/26/2015 Req'd Qty: 18.00

18

Customer:

Reference:

Approvals: Process Plan: MLJ Date: OCT 29 2015

Tooling:

Date:

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____

Date:

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
D2432	H

120

0.00

120

FLOW WATER JET

Waterjet

Memo

0.04

FLOW CNC Waterjet

Cut Blank as per D2432 File

18 ———— 10/15/11/13

130

0.01

130

HAAS CNC VERTICAL MACHINING #1

HAAS 1

Memo

0.13

HAAS CNC vertical machine #1

1-Inspect material for defects or damage prior to machining
2-Machine as per Folio and Dwg D2432 Identify as D2432F
3-Deburr

18 ———— 10/15/11/30

DAS
45 2015-11-29
9-89

140

QC2- Inspect parts off machine FAI/FAIB

0.00

140

QC

Memo

0.00

Quality Control

18 ———— 10/15/11/30

DQA: _____ Date: _____

**WORK ORDER NON-CONFORMANCE / UPDATE**

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY			
Environment ☐		No Re-verification ☐		Pressure/Forced ☐		Temperature/Cure ☐	
Design ☐		Operator ☐		Bending ☐		Set-up ☐	
Doc/Data ☐		Offset/Setup ☐		Centre Not Concentric ☐		BOM/Route ☐	
Equip/Tooling ☐		Supplier ☐		Cracks ☐		Broken/Damage/Defect ☐	
Handling/Pre ☐		Training ☐		Crimp/Kink/Ripple/Wave ☐		Inspection Incomplete/Unqualified ☐	
Material ☐		Use for Testing ☐		Cuffs ☐		Contamination ☐	
Internal Transport ☐		Poor Information ☐		Crushing ☐		Countersink ☐	
Tribal Knowledge ☐		Rushing ☐		Heat Treat ☐		Cut Too Short ☐	
LOA ☐		Product Improvement ☐		Wave/Twist in Tube ☐		Instructions Incomplete/Unclear ☐	
Substation ☐		Process Improvement ☐		Marks/Chatter ☐		Drill Holes ☐	
Past Expiry Date ☐		Manufacturing Process ☐		OTHER : ☐			
Misidentified ☐		Past Due ☐					

Work Order ID 138374***138374***

Tuesday, October 27, 2015 11:27:21 AM

Page 2

Item ID: D2432

Accept

N900040100

Setup Start

NS1

Revision ID:

Item Name: Bearpaw 19" X 24"

Stop

NS2

Start Date: 10/26/2015 Start Qty: 18.00

18

Cust Item ID:

Required Date: 10/26/2015 Req'd Qty: 18.00

18

Customer:

Reference:

Approvals:

Process Plan: _____

Date: _____

Tooling: _____

Date: _____

Run Start

NR1

QC: _____

Date: _____

SPC (Y/N): _____

Date: _____

Stop

NR2Sequence ID/
Work Center IDOperation
DescriptionSet Up/
Run Hours

Tool ID

Tool #

Plan
CodeAccept
QtyReject
QtyReject
NumberInsp.
Stamp

150

QC8- Inspect parts - second check

0.00

150

QC

Memo

0.01

Quality Control

18 _____ 215-12-2

160

Identify as per dwg & Stock Location: St 470A 0.00***160***

Packaging

Memo

0.00

Packaging

18 DEC 03 2015 DAS
9-89

170

QC21- Final Inspection - Work Order Release

0.00

170

QC

Memo

0.03

Quality Control

ML5 DEC 03 2015

ML5 DEC 03 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY			
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER :			
Misidentified	☐	Past Due	☐				

Picklist Print

Tuesday, October 27, 2015 11:27:21 AM

Page 1

Work Order ID: 138374

138374

Parent Item: D2432

D2432

Parent Item Name: Bearpaw 19" X 24"

Start Date: 10/26/2015

Required Date: 10/26/2015

Start Qty: 18.00

Required Qty: 18.00

Comments: IPP REV:A 12.10.17 AS PER DWG REV.H DD VERF:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
MUHMWB10		Purchased	No			120	sf	345.6000	3.7	66.6			

MIJHMWB10

UHMW 1" Black - 48"x120" Tivar Mfg.#52480104

**

DC 15/11/12

Location

Loc Qty

Loc Code

MAT

84

m132063

84

MAT018

261.6

m133248

261.6

71

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS <table style="width:100%; border: none;"> <tr> <td style="width:15%;">Skid-tube ☐</td> <td style="width:15%;">Cross tube ☐</td> <td style="width:15%;">Water Jet ☐</td> <td style="width:15%;">Engineering ☐</td> </tr> <tr> <td>Machining ☐</td> <td>Small Fab ☐</td> <td>Prod. Eng. Coord. ☐</td> <td>Quality ☐</td> </tr> <tr> <td>Thermoforming ☐</td> <td>Finishing ☐</td> <td>Rec/Store/Packaging ☐</td> <td>Other ☐</td> </tr> <tr> <td>Large Fab ☐</td> <td>Composite ☐</td> <td>Supplier ☐</td> <td></td> </tr> </table>						Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐	Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐	Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐	Large Fab ☐	Composite ☐	Supplier ☐																																					
Skid-tube ☐	Cross tube ☐	Water Jet ☐	Engineering ☐																																																										
Machining ☐	Small Fab ☐	Prod. Eng. Coord. ☐	Quality ☐																																																										
Thermoforming ☐	Finishing ☐	Rec/Store/Packaging ☐	Other ☐																																																										
Large Fab ☐	Composite ☐	Supplier ☐																																																											
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																						
Description Work Order Deviation				Disposition																																																									
Root Cause <table style="width:100%; border: none;"> <tr><td>Environment ☐</td><td>No Re-verification ☐</td></tr> <tr><td>Design ☐</td><td>Operator ☐</td></tr> <tr><td>Doc/Data ☐</td><td>Offset/Setup ☐</td></tr> <tr><td>Equip/Tooling ☐</td><td>Supplier ☐</td></tr> <tr><td>Handling/Pre ☐</td><td>Training ☐</td></tr> <tr><td>Material ☐</td><td>Use for Testing ☐</td></tr> <tr><td>Internal Transport ☐</td><td>Poor Information ☐</td></tr> <tr><td>Tribal Knowledge ☐</td><td>Rushing ☐</td></tr> <tr><td>LOA ☐</td><td>Product Improvement ☐</td></tr> <tr><td>Substation ☐</td><td>Process Improvement ☐</td></tr> <tr><td>Past Expiry Date ☐</td><td>Manufacturing Process ☐</td></tr> <tr><td>Misidentified ☐</td><td>Past Due ☐</td></tr> </table>		Environment ☐	No Re-verification ☐	Design ☐	Operator ☐	Doc/Data ☐	Offset/Setup ☐	Equip/Tooling ☐	Supplier ☐	Handling/Pre ☐	Training ☐	Material ☐	Use for Testing ☐	Internal Transport ☐	Poor Information ☐	Tribal Knowledge ☐	Rushing ☐	LOA ☐	Product Improvement ☐	Substation ☐	Process Improvement ☐	Past Expiry Date ☐	Manufacturing Process ☐	Misidentified ☐	Past Due ☐	FAULT CATEGORY <table style="width:100%; border: none;"> <tr> <td style="width:33%;">Pressure/Forced ☐</td> <td style="width:33%;">Temperature/Cure ☐</td> <td style="width:33%;">Power Loss/Surge ☐</td> </tr> <tr> <td>Bending ☐</td> <td>Set-up ☐</td> <td>Folio/Program ☐</td> </tr> <tr> <td>Centre Not-Concentric ☐</td> <td>BOM/Route ☐</td> <td>Grain ☐</td> </tr> <tr> <td>Cracks ☐</td> <td>Broken/Damage/Defect ☐</td> <td>Weld ☐</td> </tr> <tr> <td>Crimp/Kink/Ripple/Wave ☐</td> <td>Inspection Incomplete/Unqualified ☐</td> <td>Wrong Stock Pulled ☐</td> </tr> <tr> <td>Cuffs ☐</td> <td>Contamination ☐</td> <td>Out of Sequence ☐</td> </tr> <tr> <td>Crushing ☐</td> <td>Countersink ☐</td> <td>Off-set ☐</td> </tr> <tr> <td>Heat Treat ☐</td> <td>Cut Too Short ☐</td> <td>Mislabeled ☐</td> </tr> <tr> <td>Wave/Twist in Tube ☐</td> <td>Instructions Incomplete/Unclear ☐</td> <td>Fit/Function ☐</td> </tr> <tr> <td>Marks/Chatter ☐</td> <td>Drill Holes ☐</td> <td>Misaligned/off center ☐</td> </tr> </table>						Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Centre Not-Concentric ☐	BOM/Route ☐	Grain ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Crushing ☐	Countersink ☐	Off-set ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐
Environment ☐	No Re-verification ☐																																																												
Design ☐	Operator ☐																																																												
Doc/Data ☐	Offset/Setup ☐																																																												
Equip/Tooling ☐	Supplier ☐																																																												
Handling/Pre ☐	Training ☐																																																												
Material ☐	Use for Testing ☐																																																												
Internal Transport ☐	Poor Information ☐																																																												
Tribal Knowledge ☐	Rushing ☐																																																												
LOA ☐	Product Improvement ☐																																																												
Substation ☐	Process Improvement ☐																																																												
Past Expiry Date ☐	Manufacturing Process ☐																																																												
Misidentified ☐	Past Due ☐																																																												
Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐																																																											
Bending ☐	Set-up ☐	Folio/Program ☐																																																											
Centre Not-Concentric ☐	BOM/Route ☐	Grain ☐																																																											
Cracks ☐	Broken/Damage/Defect ☐	Weld ☐																																																											
Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐																																																											
Cuffs ☐	Contamination ☐	Out of Sequence ☐																																																											
Crushing ☐	Countersink ☐	Off-set ☐																																																											
Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐																																																											
Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐																																																											
Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐																																																											
OTHER : ☐																																																													

DART AEROSPACE LTD		Work Order: 138374
Description: Bearpaw		Part Number: D2432
Inspection Dwg: D2432	Rev: H	Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST


Inspection Sheet Drawing Dimension		Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
A	0.063 x 45°	+0.030/-0.010	0.053	✓		MJP-04	vern
B	0.200	+/-0.030	0.195	✓		MJP-08	Dial depth M12
C	0.25 x 45°	+/-0.030	0.250 x 45°	✓		MJP-04	vern
D	R0.250	+/-0.030	0.250	✓		—	Rachin gauge
E	0.250	+/-0.010	0.260	✓		MJP-04	vern
F	0.625	+/-0.030	0.645	✓		...	...
G	0.375	+0.030/-0.010	0.380	✓		↓	↓
H	0.950	+/-0.030	0.965	✓		↓	↓
I	19.000	+/-0.030	19.000	✓		MJP-07	tape
J	Ø0.260	+0.005/-0.000	0.260	✓		MJP-04	vern
K	Ø0.93	+/-0.030	0.930	✓		↓	↓
L	0.30	+0.030/-0.000	0.320	✓		↓	↓
M	23.750	+/-0.030	23.750	✓		MJP-07	tape
N	2.000	+/-0.030	2.002	✓		MJP-04	vern
O	0.38	+/-0.030	0.380	✓		...	...
P							
Q							
R							
S							
T							
U							
V							

Measured by: <i>[Signature]</i>	Audited by: <i>SL</i>	Preliminary Approval:
Date: 15/11/26	Date: 15-12-2	Date:


Rev	Date	Change	Revised by	Approved
A	04.01.09	New Issue P/O D206-559-015	KJ/RF	
B	12.07.31	Dwg Rev updated	KJ	
C	12.10.26	Dwg Rev updated	KJ	
D	13.07.18	Dimension 7.375 removed	KJ	
E	15.02.09	Dimensions revised	KJ	<i>[Signature]</i>

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER

138374 MLS
157029

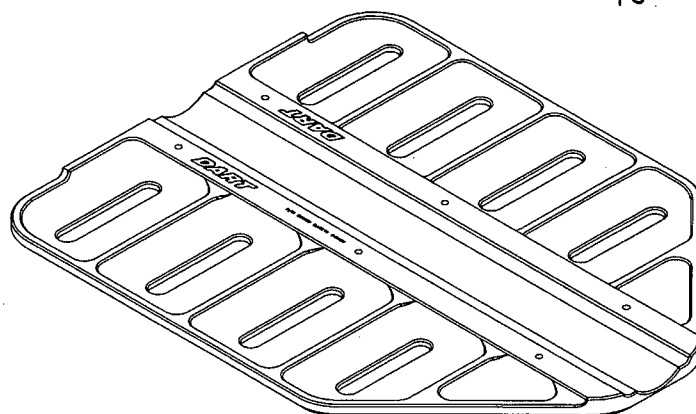


D2432F BEARPAW

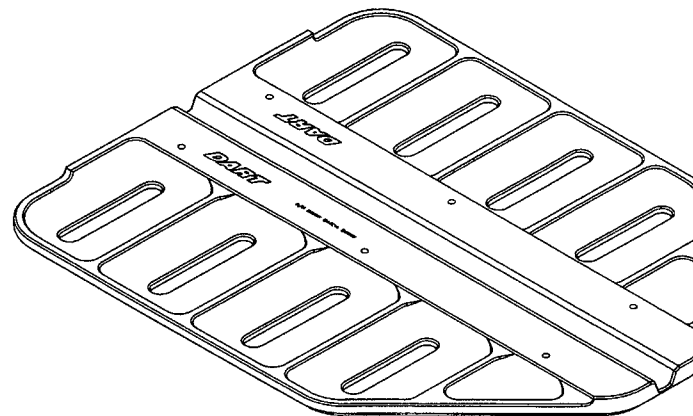

D2432-3 BEARPAW

RELEASED
R 2012-10-16

H	RIB HEIGHTS CHANGED TO CONDITION OF REV. F. SEE REV. F FOR DETAILS.	AP	12.09.24
G	UPDATE DRAWING FORMAT, REMOVED D2432B, ADD D2432-3, ADDED DIMENSION 7.52 (D1-2)	AP	12.05.02
F	CHANGE C'BORE, ADD B AND F P/N	-	98.05.12
E	CHANGE C'BORE DEPTH, BORE RADIUS	-	97.02.27
D	MOVE SLOT	-	96.06.04
C	CHANGE BORE AND C'BORE DEPTH	-	96.03.26
B	RE-DESIGN	-	96.01.24
A	NEW ISSUE	-	95.10.31
REV.	DESCRIPTION	BY	DATE
DESIGN	LE	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AP		
CHECKED	ALS	DRAWING NO.	REV. H
MFG. APPR.	at	D2432	SHEET 1 OF 3
APPROVED	AP	TITLE	SCALE
DE APPR.	at	BEARPAW	NTS
DATE	12.09.24	COPYRIGHT © 1998 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR DISCLOSED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	

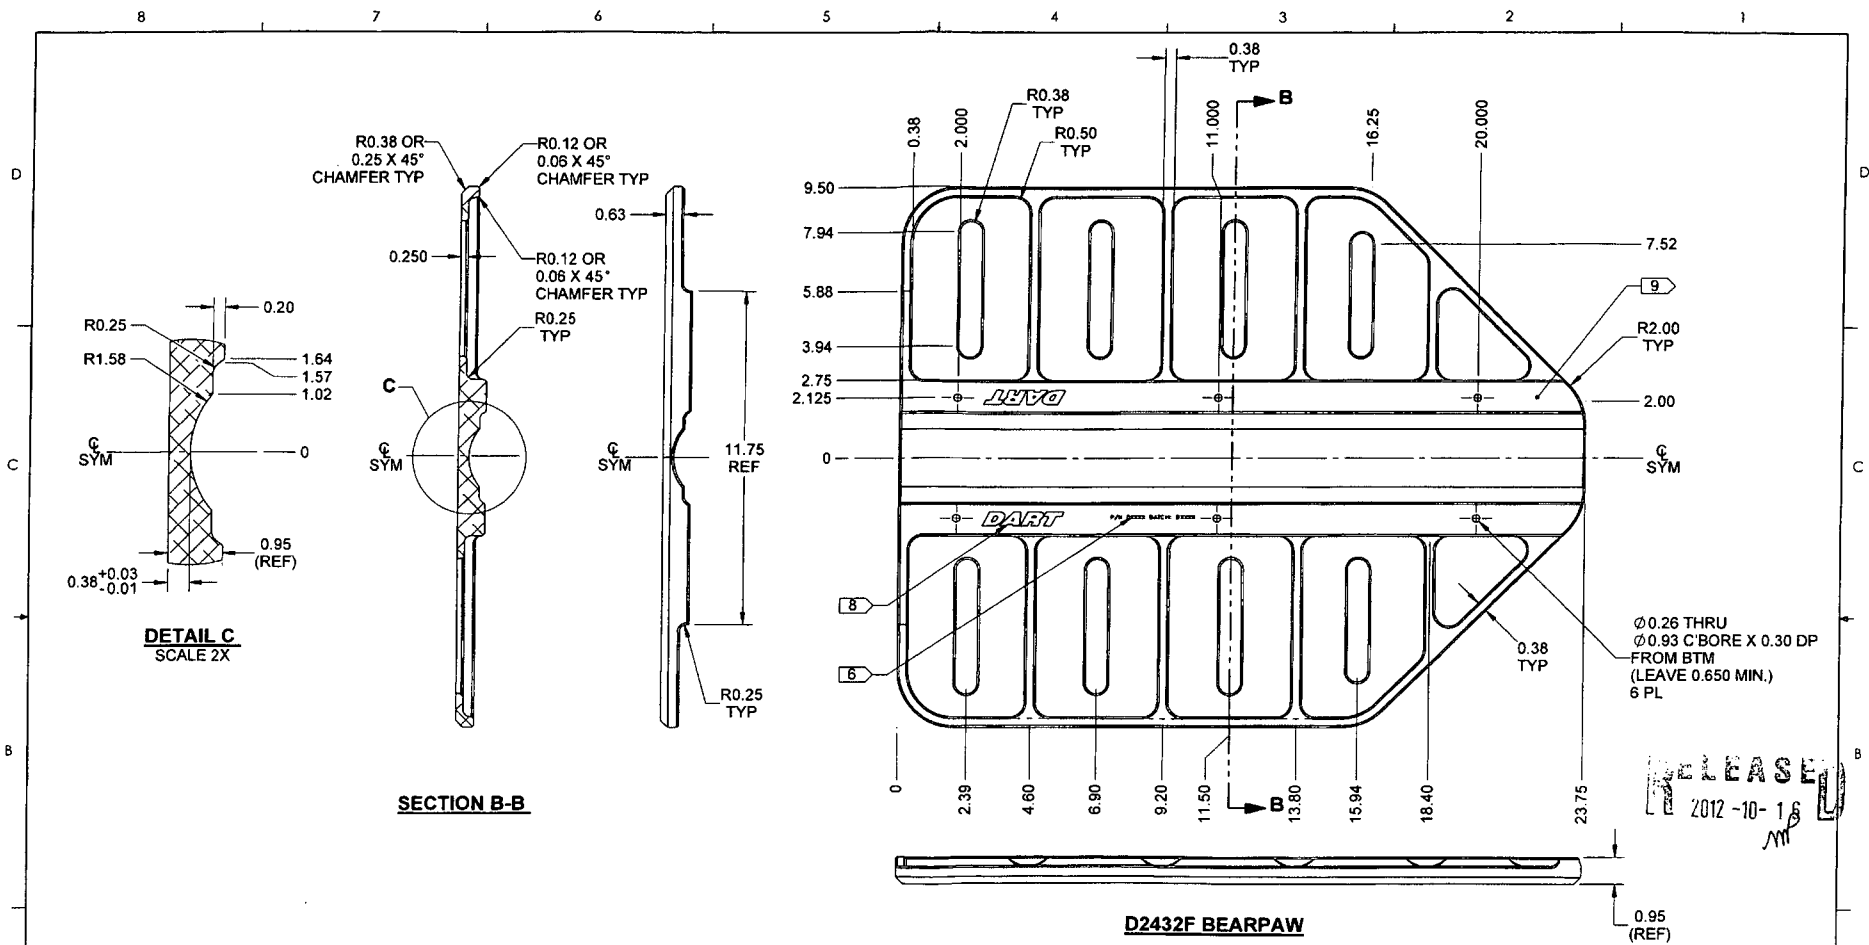

NOTES:

- 1) MATERIAL: UHMW BLACK TIVAR 1000 VIRGIN MATERIAL, 1.000 THICK MACHINED TO 0.950 (REF DART SPEC. MUHMWB10)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: ENGRAVE PART NUMBER "D2432" AND BATCH NUMBER "BXXXXX" IN ACCORDANCE WITH QSI 044 METHOD 6.3
- 7) WEIGHT: 5.87 lbs
- 8) ENGRAVE DART LOGO TO MAX DEPTH OF 0.012
- 9) APPLY 0.06 x 45° CHAMFER TO ALL EDGES ON SIDE SHOWN UNLESS OTHERWISE INDICATED
- 10) PROFILE PER DRAWING FILE "D2434F-REVH.STP"

DESIGN	LE	DART AEROSPACE LTD	
DRAWN	AP	HAWKESBURY, ONTARIO, CANADA	
CHECKED	ASS	DRAWING NO.	REV. H
MFG. APPR.	21	D2432	SHEET 2 OF 3
APPROVED	10	TITLE	SCALE
DE APPR.	10	BEARPAW	NTS
DATE	12.09.24	COPYRIGHT © 1986 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

RELEASE
2012-10-16

